


MAINTAINING TRAFFIC LEGEND

- DETOUR ROUTE
- PROJECT LOCATION
- TYPE III BARRICADE
- TEMPORARY SIGN

ESTIMATED QUANTITIES

SIGN	SIZE	AREA PER SIGN (SFT)	NUMBER	TOTAL AREA (SFT)
R1-1	36"x36"	9	4	36
R5-1	36"x36"	9	6	54
SIGN, TYPE A, TEMP, PRISMATIC				
G20-2	48"x24"	8	2	16
M4-8a	24"x18"	3	1	3
M4-9L	30"x24"	5	5	25
M4-9R	30"x24"	5	2	10
M4-9S	30"x24"	5	1	5
M4-10L	48"x18"	6	1	6
R5-18c	48"x48"	16	2	32
R6-1L	36"x12"	3	4	12
R6-1R	36"x12"	3	2	6
R11-2	48"x30"	10	1	10
W20-1	48"x48"	16	6	96
W20-2	48"x48"	16	1	16
W20-3	48"x48"	16	1	16
SIGN, TYPE B, TEMP, PRISMATIC				
D3-1 (12TH ST)	30"x12"	2.5	9	22.5
R-VAR (US-31 & MAPLE)	90"x36"	22.5	3	67.5
R-VAR (MAPLE & US-31)	66"x36"	16.5	3	49.5
W16-8PV (ON 12TH ST)	48"x15"	5	4	20
SIGN, TYPE B, TEMP, PRISMATIC, SPECIAL				
BARRICADE, TYPE III, HIGH INTENSITY, DOUBLE SIDED, LIGHTED				
4				

SEE NOTE SHEET FOR QUANTITIES.
SEE SHEET 28 FOR SIGN SPECIAL DETAILS.

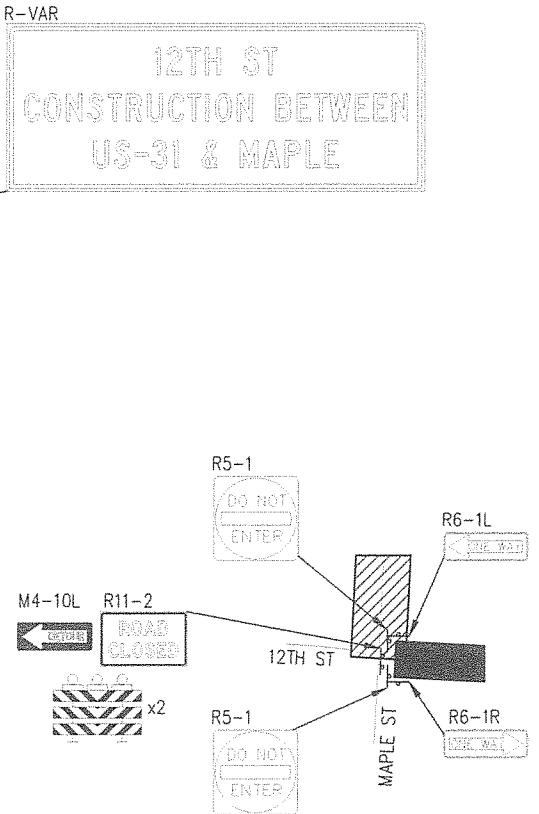

11/16/2018 12:20 PM nathynn

FINAL PLAN REVISIONS

NO.	DATE	AUTH	DESCRIPTION

Spicer group

SAGINAW OFFICE
230 S. Washington Ave.
Saginaw, MI 48607
Tel. 989-754-4717
Fax. 989-754-4440
www.SpicerGroup.com

0 VERT. (FT) N/A
0 HORIZ. (FT) N/A

SGI PROJECT NO: 120924SG2013
DATE: NOVEMBER, 2018
FILE: LP_MOT.DWG

CS: 51000
JN: 200761

MAINTAINING TRAFFIC
12TH STREET

DRAWING SHEET
DTR1 27

PROGRESS SCHEDULE

Information required by MDOT in order to establish a construction schedule.

Distribution: Original - Project files

FILE 101

CONTROL SECTION STUL 51000	JOB NUMBER 200761A	<input checked="" type="checkbox"/> INITIAL	<input type="checkbox"/> UPDATE
PROPOSAL ITEM NUMBER 1903-069	LETTING DATE March 1, 2019		

OUTLINE OF PROPOSED ORDER OF WORK FOR CONTROLLING WORK ITEMS.

CONTROLLING WORK ITEM <input type="checkbox"/> CALENDAR DAY <input type="checkbox"/> WORK DAY <input checked="" type="checkbox"/> CALENDAR DATE	ATTACHMENT <input type="checkbox"/> CRITICAL PATH <input type="checkbox"/> BAR CHART <input type="checkbox"/> LINEAR SCHEDULE	DURATION OF CONTROLLING OPERATION	
		START (Date/Work Day)	COMPLETE (Date/Work Day)
Mobilization		06/03/19	06/05/19
Removals		06/06/19	06/11/19
Subgrade Undercutting		06/11/19	06/14/19
Sand Subbase		06/14/19	06/19/19
Storm Sewer		06/19/19	07/01/19
Fire Hydrant		07/01/19	07/03/19
Aggregate Base		07/03/19	07/10/19
Concrete Drive		07/10/19	07/12/19
Concrete Curb		07/12/19	07/19/19
Concrete Sidewalk		07/19/19	07/24/19
Paving		07/24/19	08/01/19
Pavement Markings		08/01/19	08/08/19
Signs		08/09/19	08/15/19
Restoration		08/15/19	08/24/19

REMARKS:

No work shall commence prior to June 3, 2019.
 All contract work must be complete on or before August 24, 2019.
 The final project completion date for the project is September 28, 2019 to accommodate turf establishment.
 No work on Independence Day holiday, 3:00pm Wednesday 7/3/19 to 6:00am Monday 7/8/19.
 No work on Labor Day weekend, 3:00pm Friday 8/30/19 to 6:00am Tuesday 9/3/19.

CONTRACT COMPLETION 09/28/19	Conformance with progress clause and proposal (Maintain traffic Requirements) <input checked="" type="checkbox"/> Yes		
WORKDAYS	Overlapping dates? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes. If yes, attach justification		
OPEN TO TRAFFIC DATE(S) WORKDAYS	If A + B bid or rental (lane/bridge/ramp), is schedule in accordance with contract? <input type="checkbox"/> Yes		
A + B bid ? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes. If yes, enter date(s): _____	Incentive / Disincentive? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes		
Lane/Bridge/Ramp rental <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes	If yes, enter maximum total incentive amount: \$ _____		
CONTRACTOR NAME (PRINT) Elmer's Crane and Dozer, Inc.	LOCAL AGENCY	DATE	
CONTRACTOR SIGNATURE Steve Folkersma	DATE 05/21/19	MDOT APPROVAL - CONSTRUCTION/PROJECT ENGINEER (Signature)	DATE
